

Project Name	: EMR FTTH PROJECT
Cluster Name	: SF Telaga Pasir Raya RW 12
Cluster ID	:
ATP Date	: 15.02.2024

No	Defect Item	Target Date	Repaired Date	Sign (customer)
	NO FRANCHISE			

Responsible Vendor

Name: Subag 70

ID: [Signature]

Signature: [Signature]

Date: 15-06-29

Responsible Customer  
Name: thattamat # 15/29  
ID: 15/29  
Signature: [Signature]  
Date: 02.

Responsible Vendor  
Name: Subany 70  
ID: [Signature]  
Signature: [Signature]  
Date: 15-06-24

Responsible Customer  
Name: Robert F. 11/29/02  
ID: [Signature]  
Signature  
Date:

# ACCEPTANCE TEST PROCEDURE





For  
EMR GPON Project

PT Eka Mas Republik

Subfeeder Name : SF TELAGA PASIR RAYA RW 12

Document Prepared by YOFC and Approved by EMR

YOFC Representation: Subagyo  15/24  
02

EMR Representation: Rahmat Paudi  15/24  
02



YOFC International Indonesia  
2021



Sub Optical System					
Integration, Testing & Commissioning					
Monitoring (Testcomm / Uj Tarima):		core			
a) OPM OLT - FAT		core	6		
b) OPM ODF - FDT		core			
c) OPM FDT - FAT					
Sub Total Aktiva, Integrasi, Testing & Commissioning					
Installation		meter	1.004	1.004	
Design (Asplan)		set per site	1	1	
Auto Drawing A1 (1 set soft + 3 set copy + soft copy), KMZ, BOQ		set per site	1	1	
Dokumentasi					
Sub Total Documentation					
3 Others					
a) Project Management		meter	1.004	1.004	
Sub Total Project Management Fee					
4 Warehouse					
a) Warehouse		ls	1	1	
b) Transportation to site		ls	1	1	
Sub Total Warehouse					
5 Extended Warranty & Maintenance (After 1 year basic Warranty & Maintenance) - (Optional)					
a) Warranty & Maintenance ODN per year		ls			
Sub Total Extended Warranty & Maintenance					
6 Tools and Test Equipment (Optional)					
a) Optical Power Meter 1310nm, 1490nm, 1550nm		unit			
b) OTDR (Optical Time Domain Reflectometer)		unit			
c) Fusion Splicer		unit			
Sub Total Tools and Test Equipment					
7 Training - (Optional)					
a) FTTH Local Training		person			
b) FTTH Training Certified by FTTH Council		person			
Sub Total Training					
8 Bank Garansi (Optional)- di DKI untuk UG saja					
a) Jaminan Pelaksanaan Perbaikan berupa Bank Garansi		qty			
b) Jaminan Pemeliharaan berupa Bank Garansi		lot			
SUB TOTAL Bank Garansi (Optional)					
Total ODN, OSP, Aktiva, Instalasi, Integrasi, Testing & Dokumentasi					
Grand Total					
Cost per Home Pass (IDR)					
Cost per Home Pass (USD)					

VENDOR

RESPONSIBLE VENDOR

NAME

ID

SIGNATURE

DATE

Subang  
15/01/20

PT EKA MAS REPUBLIC

RESPONSIBLE CUSTOMER


NAME

ID

SIGNATURE

DATE

15/29  
02

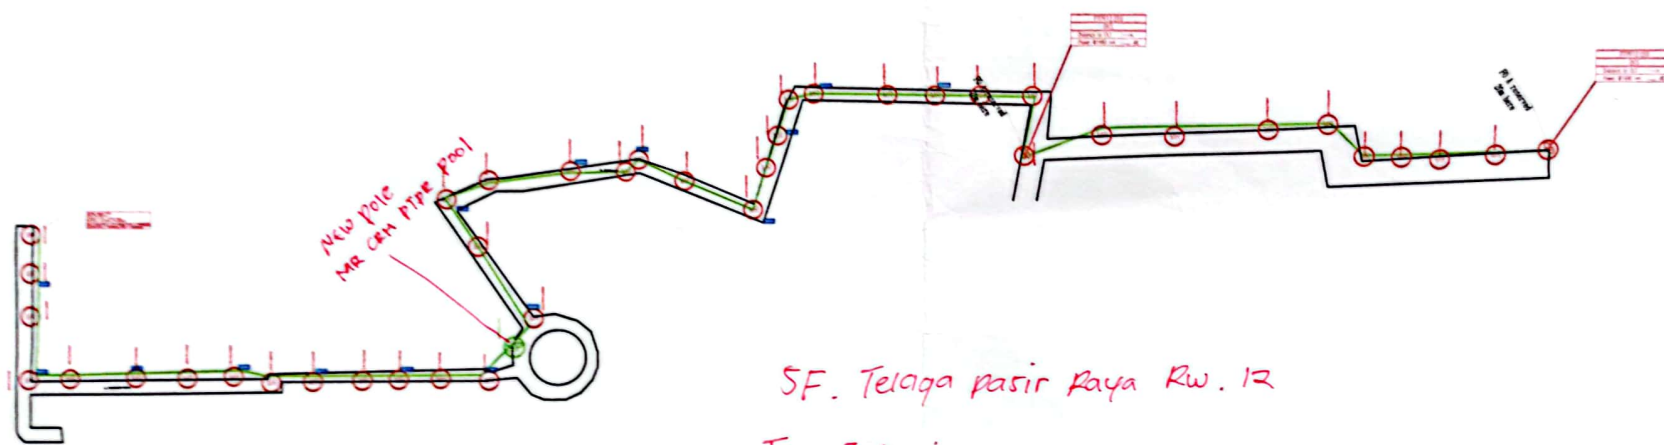

SF. Telaga pasir Raya Rw. 12

- Tiang 7-4inchi : 1 Batang
- Kabel 24. Core : 1.542 Meter
- Clampole : 41 pcs
- Deadend : 54 pcs
- Suspensi : 14 pcs
- JC FDT 01 : 6. Core
- JC Ex 1 : 12 Core
- JC Ex 2 : 12 Core
- JC Ex 3 : 12 Core
- JC Ex 4 : 12 Core
- FDT 02 : 7 Core

Hand 15/24  
Ass.S.

15/24

15/24  
Pakmanat

# LEGEND

	HUB / CENTRAL OFFICE		HANDHOLE 40x40
	SUB HUB / OPTICAL LINE TERMINAL		UNDERGROUND PEDESTAL
	FIBER DISTRIBUTION TERMINAL		PROPOSES NEW
	FIBER ACCESS TERMINAL / FAT / SPLITTER CONFIG		PROPOSES NEW
	OPTICAL TERMINATION BOX		GARDU PLN
	HANDHOLE BURIED 130		RUMAH YABEL
	ONT-RES (RESIDENTIAL) OPTICAL NETWORK TERMINAL		LARGE TEE RW
	ONT-MCU (BUILDING) OPTICAL NETWORK TERMINAL		CABLE RISER
	FIBER OPTIC CLOSURE		BORING ASPM
	FIGURE EIGHT / FIBER SPIKE CUL		BORING TANK
	TRENCHING		GALI TANAH

## CABLE TYPE

AERIAL STRAND	FIBER 12/2T
UNDERGROUND STRAND	FIBER 24/4T
LC DROP DUCT	FIBER 36/3T
RIDER CABLE ROUTE	FIBER 12/2T
FAI AREA LINE	FIBER 36/3T
	FIBER 144/12T
	FIBER 288/24T

## AERIAL

No.	DATE	REVISION

MyRepublic  
Grafika PIM  
Jl. Terusan Cikarang No. 1000  
Cikarang Barat 13133  
Telp. +6221 319 2826

PT. HOKI INDAH  
GPR, Tower 1000, 1000, 1000  
S. Purnomo, K. S. Purnomo, 1000  
Telp. +6221 319 2826

SUB FEEDER PERUMAHAN TELAGA PASIR RAYA RW 12

AS PLAN DRAWING FTTH NETWORK

## DRAWING SIGN & CHECK

DESIGN SUMMARY	
SUB FEEDER PERUMAHAN TELAGA PASIR RAYA RW 12	
LINE (FIBER 24C/2T)	100 m
TOTAL NEW 7W 5" POLE	1 units
TOTAL NEW 7W 4" POLE	1 units
TOTAL EXT POLE MR	33 units
TOTAL EXT POLE LINEMAN	1 units
PD JOINT CLOSURE INLINE 144 CORE	1 units
PD JOINT CLOSURE INLINE 48 CORE	1 units
TOTAL DUCT ROUTE DIST	100 m
TOTAL DROP DUCT ROUTE DIST	100 m
TOTAL AERIAL ROUTE DIST	100 m
TOTAL STRAND WIRE ROUTE DIST	100 m

## APPROVAL MATRIX

Planning Dept	Vendor/contractor
---------------	-------------------

North Arrow

N T S
